



附表14 主計畫網圖

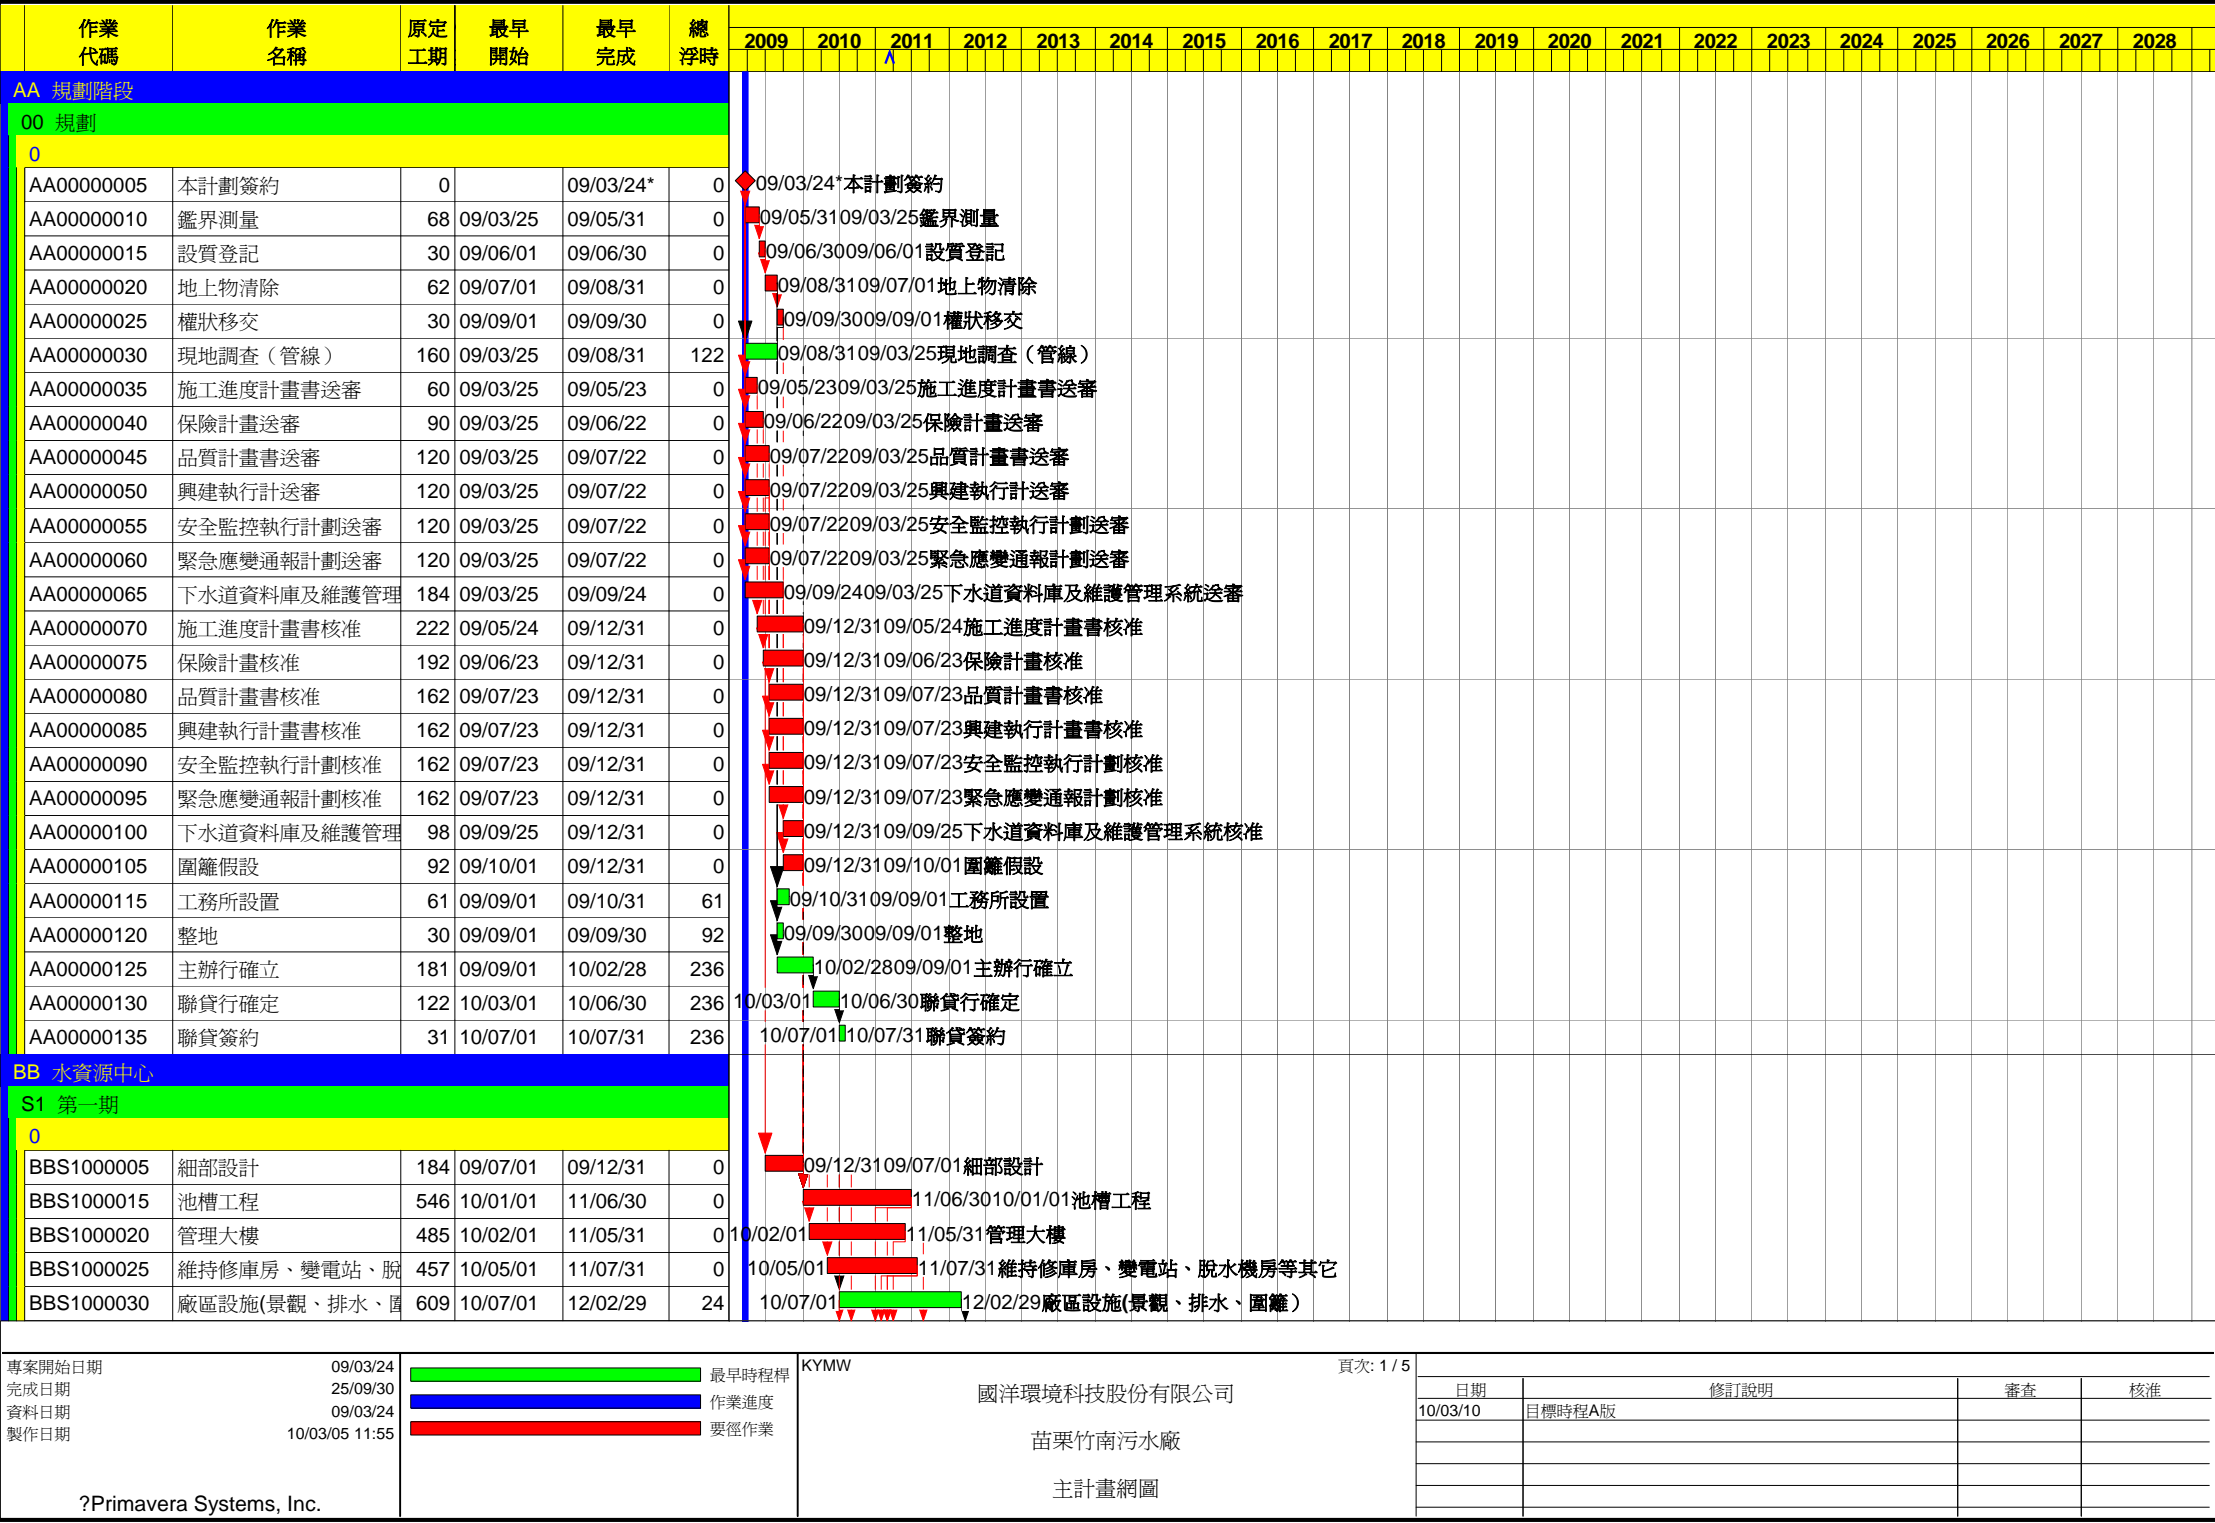


附表14 主計畫網圖

作業代碼	作業名稱	原定工期	最早開始	最早完成	總浮時																													
						2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028									
	BBS1000040	機械設備(採購)	426	10/07/01	11/08/30	0	10/07/01																											
	BBS1000045	機械設備(安裝)	242	11/02/01	11/09/30	0		11/02/01																										
	BBS1000050	管線工程	365	11/01/01	11/12/31	0		11/01/01																										
	BBS1000060	儀控電力(採購)	365	10/09/01	11/08/31	0		10/09/01																										
	BBS1000065	電力工程(含高壓變電)	245	11/03/01	11/10/31	0		11/03/01																										
	BBS1000070	儀表控制工程	184	11/07/01	11/12/31	0		11/07/01																										
	BBS1000075	試車計畫	122	11/04/01	11/07/31	0		11/04/01																										
	BBS1000080	整體維護計畫	92	11/07/01	11/09/30	176		11/07/01																										
	BBS1000085	整體設備功能測試評估計	92	11/07/01	11/09/30	84		11/07/01																										
	BBS1000090	營運管理計畫書	92	11/10/01	11/12/31	84		11/10/01																										
	BBS1000095	試車(單體)	123	11/10/01	12/01/31	0		11/10/01																										
	BBS1000100	試車(系統)	121	11/11/01	12/02/29	0		11/11/01																										
	BBS1000105	試車(處理效率)	53	12/02/01	12/03/24	0			12/02/01																									
	BBS1000110	完工(證照申請)	206	11/09/01	12/03/24	0		11/09/01																										
	BBS1000115	完工(成果報告)	53	12/02/01	12/03/24	0			12/02/01																									
	BBS1000120	開始營運	0		12/03/24	0				12/03/24																								
S2 第二期																																		
0																																		
BBS2000005	擴廠計畫書	61	13/05/01*	13/06/30	1,850				13/05/01*																									
BBS2000010	細部設計	245	13/05/01	13/12/31	1,850			13/05/01																										
BBS2000015	土建工程	669	14/01/01	15/10/31	1,850				14/01/01																									
BBS2000020	機械管線工程	549	14/05/01	15/10/31	1,850				14/05/01																									
BBS2000025	儀電工程	488	14/07/01	15/10/31	1,850				14/07/01																									
BBS2000030	試車(單體)	122	15/08/01	15/11/30	1,850					15/08/01																								
BBS2000035	試車(系統)	122	15/09/01	15/12/31	1,850					15/09/01																								
BBS2000040	試車(處理效率)	61	15/11/01	15/12/31	1,850					15/11/01																								
BBS2000045	完工(成果報告)	60	16/01/01	16/02/29	1,850					16/01/01																								
S3 第三期																																		
0																																		
BBS3000005	擴廠計畫書	92	20/05/01*	20/07/31	1,544																													
BBS3000010	細部設計	245	20/05/01	20/12/31	1,544																													
BBS3000015	土建工程	669	21/01/01	22/10/31	1,544																													
BBS3000020	機械管線工程	549	21/05/01	22/10/31	1,544																													
BBS3000025	儀電工程	488	21/07/01	22/10/31	1,544																													
BBS3000030	試車(單體)	122	22/08/01	22/11/30	1,544																													
BBS3000035	試車(系統)	122	22/09/01	22/12/31	1,544																													
BBS3000040	試車(處理效率)	61	22/11/01	22/12/31	1,544																													
專案開始日期			09/03/24				KYMW										頁次: 2 / 5																	
完成日期			25/09/30														國洋環境科技股份有限公司																	
資料日期			09/03/24														苗栗竹南污水廠																	
製作日期			10/03/05 11:55														主計畫網圖																	
</																																		

附表14 主計畫綱圖

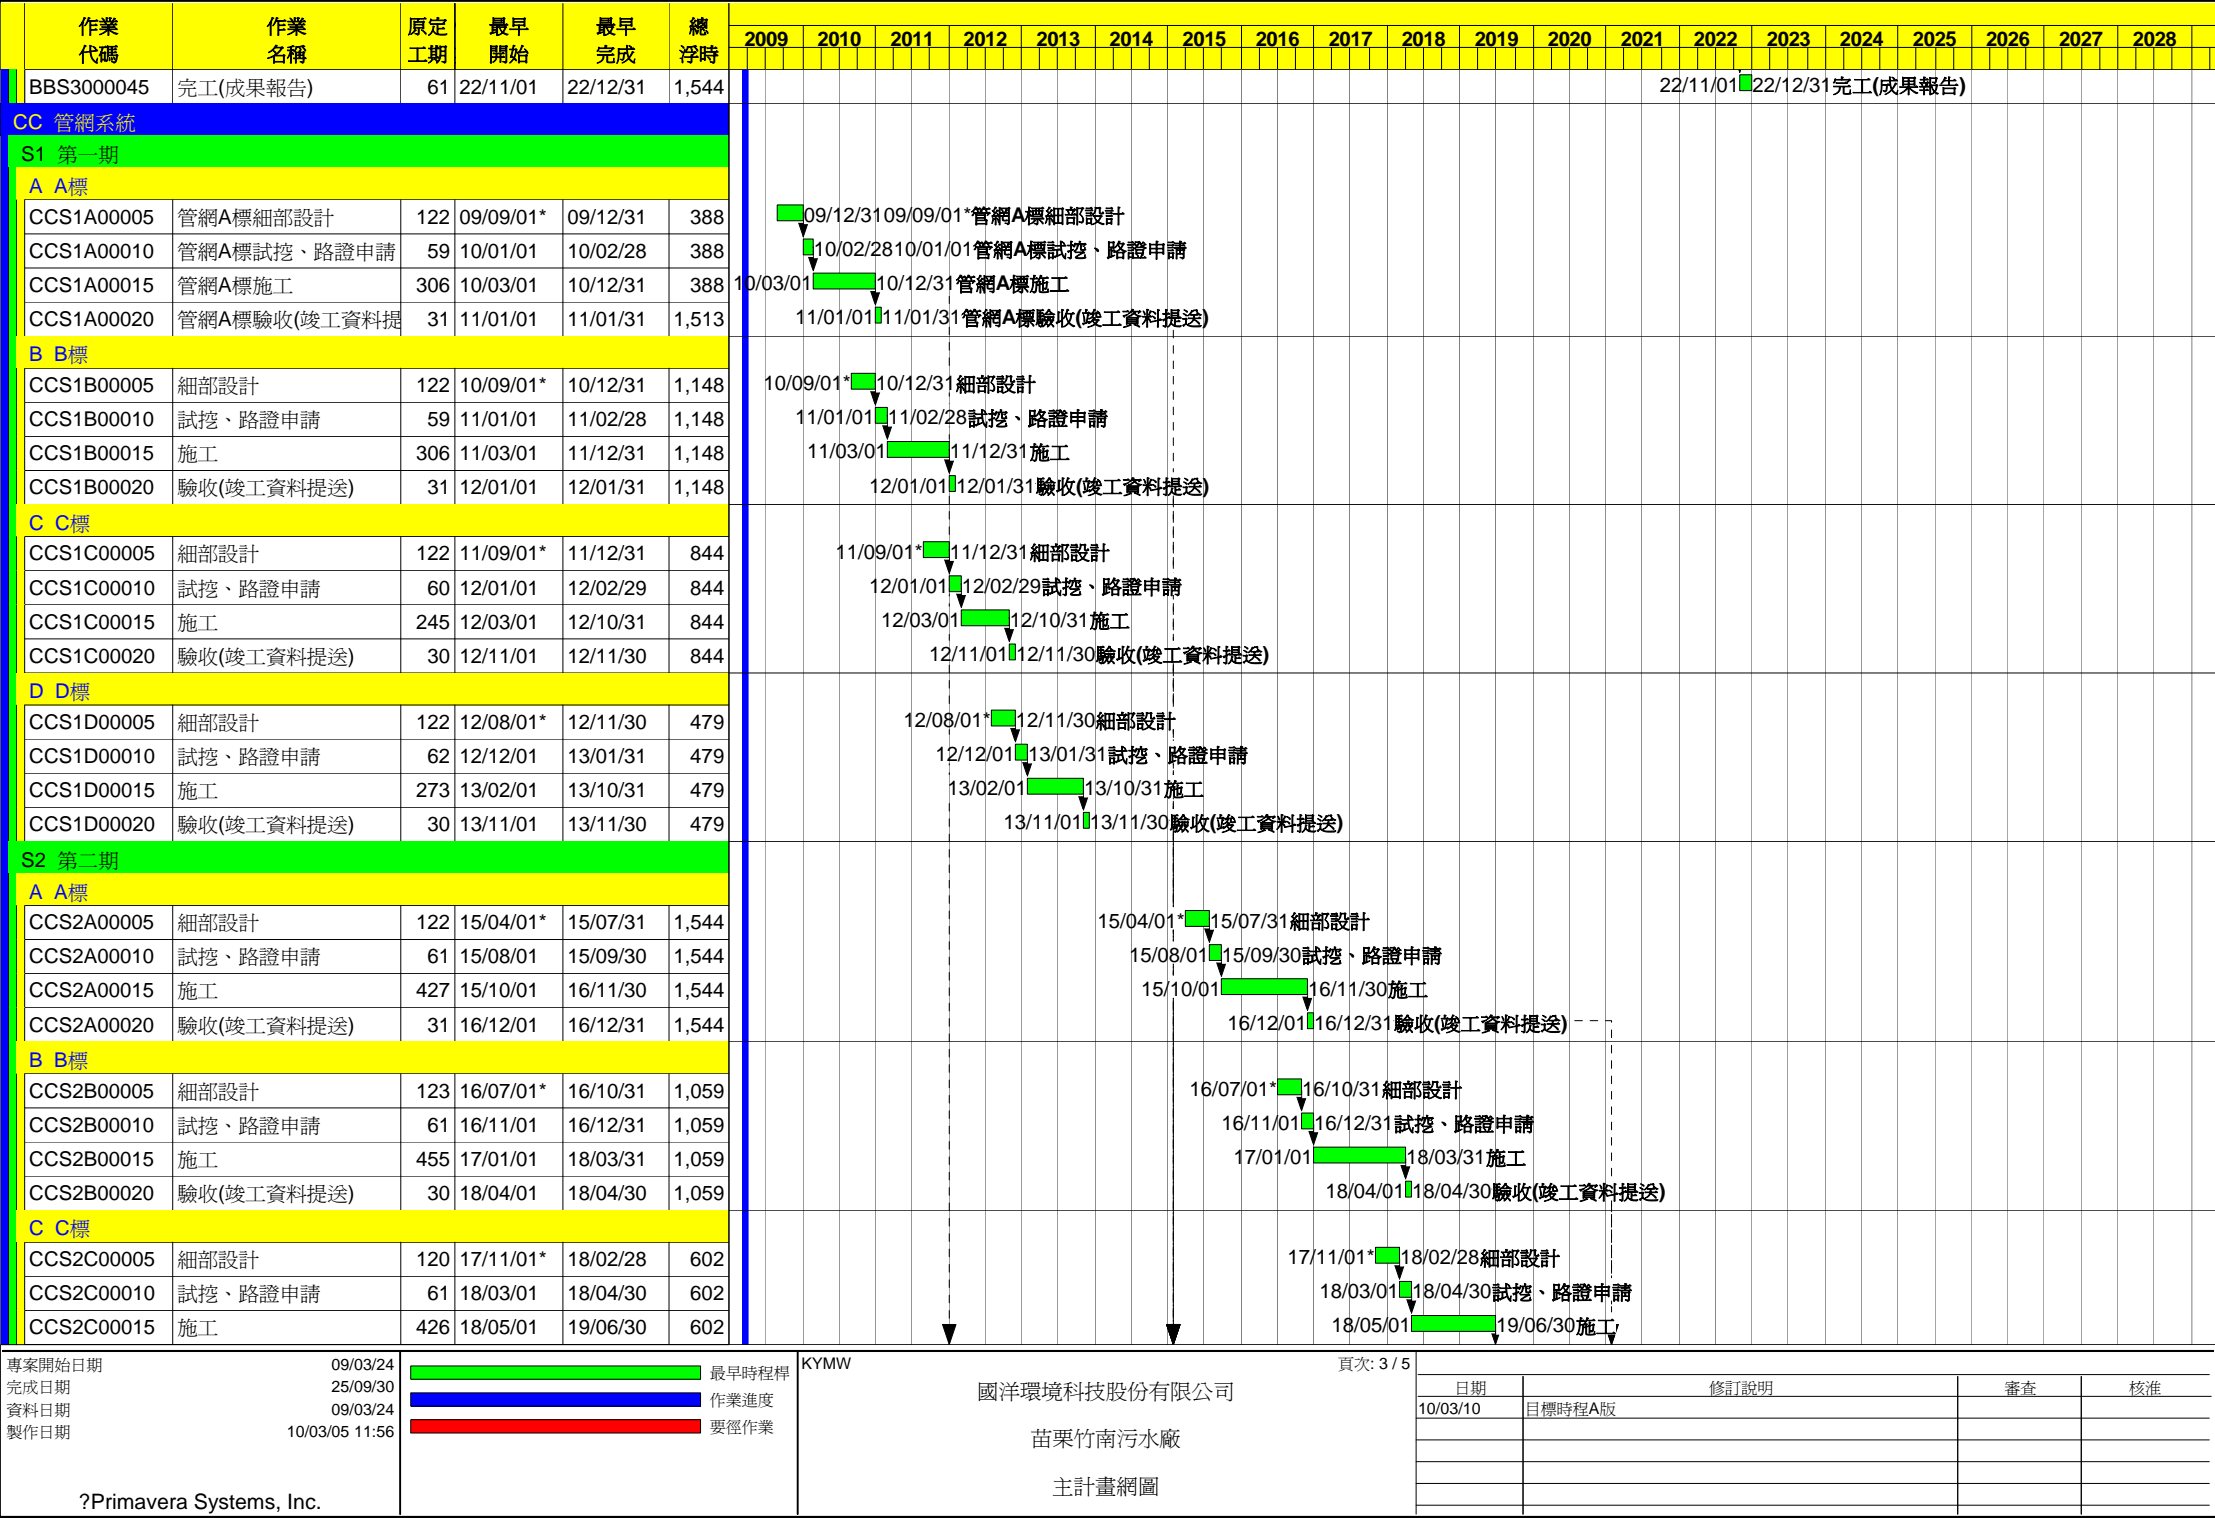

附表14 主計畫網圖

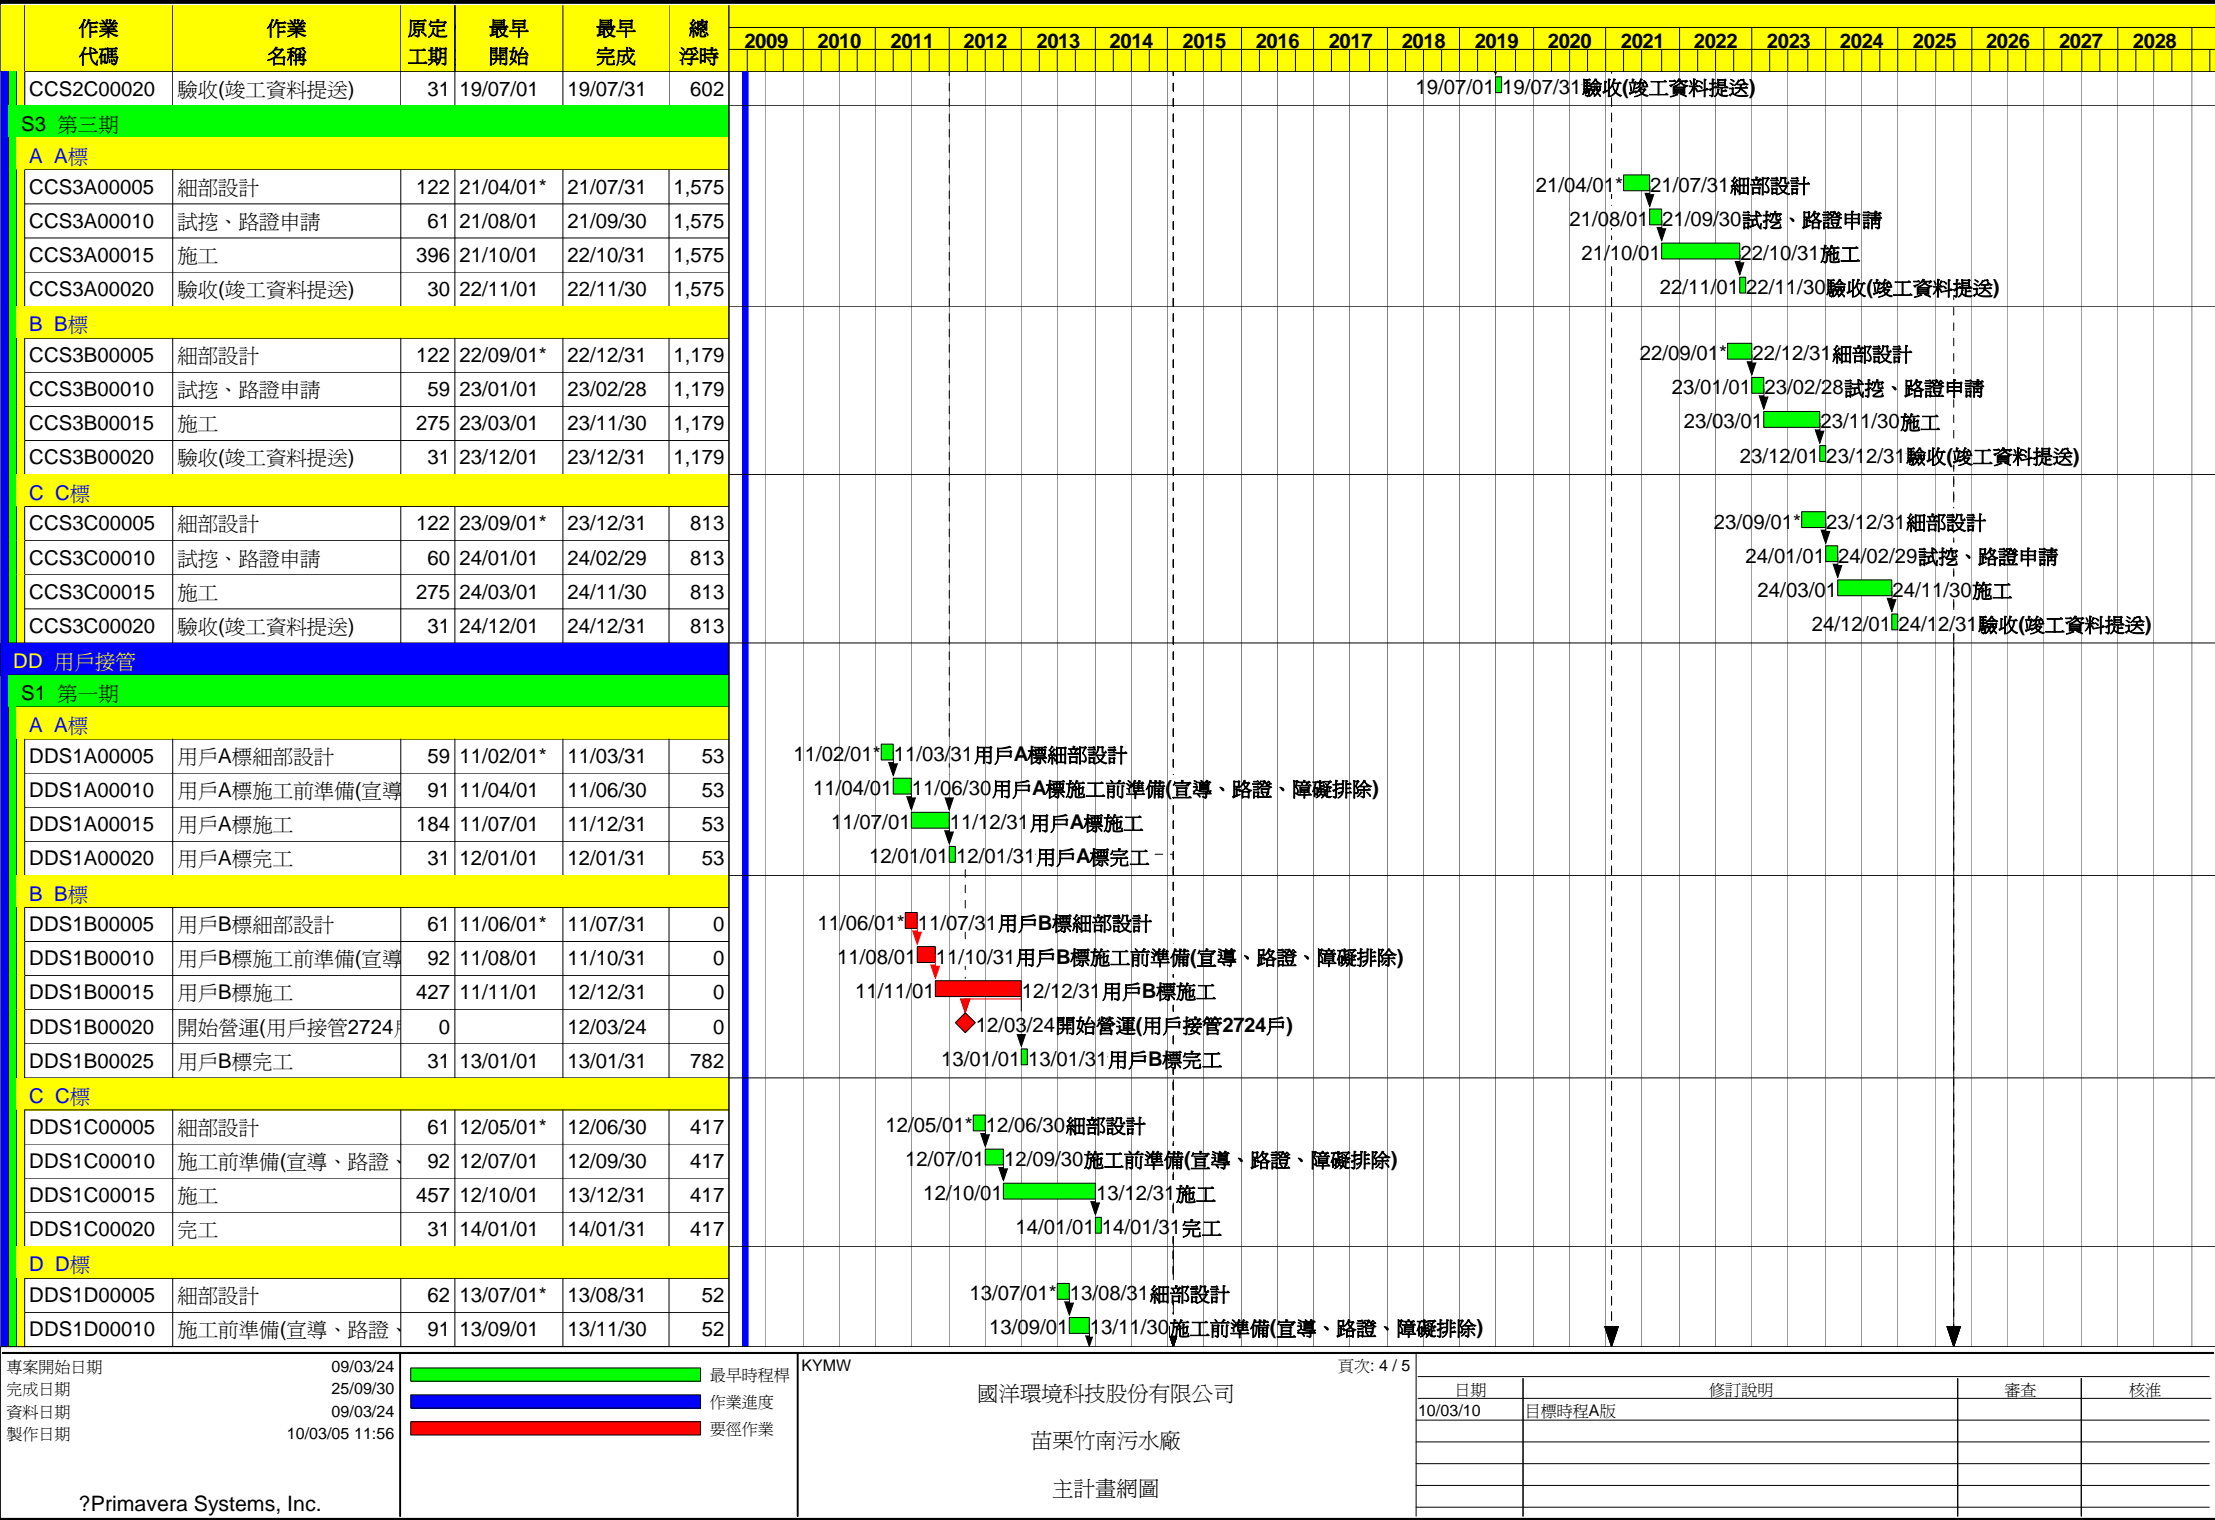

附表14 主計畫網圖

作業代碼		作業名稱	原定工期	最早開始	最早完成	總浮時	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028
DDS1D00015	施工		396	13/12/01	14/12/31	52						13/12/01														
DDS1D00020	完工		31	15/01/01	15/01/31	52						15/01/01														
DDS1D00025	第一期完工(累計16342戶)		0		15/01/31	52							15/01/31													
S2 第二期																										
A A標																										
DDS2A00005	細部設計		61	16/06/01*	16/07/31	1,148							16/06/01*													
DDS2A00010	施工前準備(宣導、路證、		92	16/08/01	16/10/31	1,148							16/08/01													
DDS2A00015	施工		426	16/11/01	17/12/31	1,148							16/11/01													
DDS2A00020	完工		31	18/01/01	18/01/31	1,148								18/01/01												
B B標																										
DDS2B00005	細部設計		61	17/11/01*	17/12/31	663								17/11/01*												
DDS2B00010	施工前準備(宣導、路證、		90	18/01/01	18/03/31	663								18/01/01												
DDS2B00015	施工		395	18/04/01	19/04/30	663								18/04/01												
DDS2B00020	完工		31	19/05/01	19/05/31	663									19/05/01											
C C標																										
DDS2C00005	細部設計		61	19/08/01*	19/09/30	52										19/08/01*										
DDS2C00010	施工前準備(宣導、路證、		92	19/10/01	19/12/31	52										19/10/01										
DDS2C00015	施工		366	20/01/01	20/12/31	52										20/01/01										
DDS2C00020	完工		31	21/01/01	21/01/31	52											21/01/01									
DDS2C00025	第二期完工(累計32577戶)		0		21/01/31	52												21/01/31								
S3 第三期																										
A A標																										
DDS3A00005	細部設計		61	22/08/01*	22/09/30	1,088													22/08/01*							
DDS3A00010	施工前準備(宣導、路證、		92	22/10/01	22/12/31	1,088													22/10/01							
DDS3A00015	施工		425	23/01/01	24/02/29	1,088													23/01/01							
DDS3A00020	完工		31	24/03/01	24/03/31	1,088														24/03/01						
B B標																										
DDS3B00005	細部設計		62	23/12/01*	24/01/31	874														23/12/01*						
DDS3B00010	施工前準備(宣導、路證、		90	24/02/01	24/04/30	874														24/02/01						
DDS3B00015	施工		153	24/05/01	24/09/30	874														24/05/01						
DDS3B00020	完工		31	24/10/01	24/10/31	874														24/10/01						
C C標																										
DDS3C00005	細部設計		62	24/12/01*	25/01/31	540															24/12/01*					
DDS3C00010	施工前準備(宣導、路證、		89	25/02/01	25/04/30	540															25/02/01					
DDS3C00015	施工		123	25/05/01	25/08/31	540															25/05/01					
DDS3C00020	完工		30	25/09/01	25/09/30	540															25/09/01					
DDS3C00025	第三期完工(累計43131戶)		0		25/09/30	540																25/09/30				

專案開始日期09/03/24

完成日期25/09/30

資料日期09/03/24

製作日期10/03/05 11:56

最早時程桿

作業進度

要徑作業

KYMW

國洋環境科技股份有限公司

苗栗竹南污水廠

主計畫網圖

頁次: 5 / 5

日期	修訂說明	審查	核准
10/03/10	目標時程A版		

?Primavera Systems, Inc.
